

# THE UNIVERSITY of TEXAS SYSTEM OFFICE of FACILITIES PLANNING and CONSTRUCTION

Nine Universities, Six Health Institutions, Unlimited Possibilities.


## 302-244 Campus Landscape Enhancement Project

The University of Texas at Dallas

## Executive Summary Report

### Project Description

The Project includes enhancement of the campus entrance along University Parkway from Campbell Road and central core campus enhancements with the priority being the central plaza surrounded by McDermott Library, the Student Union, the Founders Building and the Green Center. Enhancements will combine major signature visual themes, structural elements including water features, elegant, functional pedestrian ways with attractive vistas, attractive, functional entrances to current buildings, and specific subspaces embodying combinations of functionality and aesthetic interest that will serve as powerful attractors for students, faculty and staff.

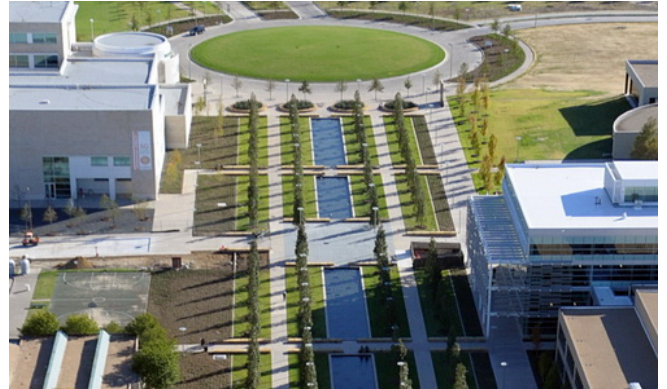

### Project Information

Project Status:	Active
Project Delivery Method:	Construction Manager at Risk
CIP Project Type:	Renovation
Gross and Assignable Square Feet:	GSF: 801,691      ASF: 0
"44 Initiative: Project:	No
Phase and Estimated % Complete:	Construction - 100%
OFPC RPM, SPM, PM, RCM, IM:	Salcher, Lund, Lund, Yauger, NA
Architecture Firm:	Peter Walker & Partners LA, Inc
Construction Firm:	Austin Commercial, Inc

### Project Budget

Construction Services:	\$ 21,615,614	at \$ 27 / GSF
Total Project Cost:	\$ 33,000,000	at \$ 41 / GSF

### Project Funding

Gifts	\$ 21,200,000
Revenue Financing System Bonds	\$ 5,700,000
Unexpended Plant Fund	\$ 6,100,000

### Project Schedule

BOR/Chancellor DD Approval	05/14/2008
Issue NTP - Construction	10/30/2008
Achieve Substantial Completion	11/18/2010
Achieve Operational Occupancy	11/18/2010

### Project Remarks

1. 302-244 CLEP Phase 1 SC for the project in its entirety achieved on November 18, 2010.
2. TPC increased by \$2M to \$33M on 10/19/2011.
3. ASP #22 will cover Landscape Design Fees to complete CD's and CA on remaining scope of work for Campus Landscape Enhancement Project Phase II, 302-765.
4. 302-765 CLEP Phase II issued NTP for N. Mall Demolition on 12/09/2013
5. 302-765 CLEP Phase II Issued NTP for Area A Construction on 08/05/2014
6. Area A North Mall SC projected for 01/31/2015. Remainder of Project SC 10/04/2015.

### Board Approvals

Request for Approval to Increase TPC by \$2,000,000.00 approved by Chancellor Cigarroa on 10/19/11.
