


302-323 Student Services Building
 The University of Texas at Dallas

Executive Summary Report

Project Description

This facility will provide a "one-stop" center housing the primary departments which students, parents and prospective students need to visit and do business within the course of their relationship with UT Dallas. The building will accommodate the following departments: Disability Services, Bursar Office, Financial Aid Office, Office of Registrar, Career Center, International Student Services, LSL/NSP, Multicultural Center, Office of Dean of Students, Health Center, Student Affairs Communication, Facility Support, and Counseling Center. The building will be a four-story structure with "one-stop" service on the ground floor.

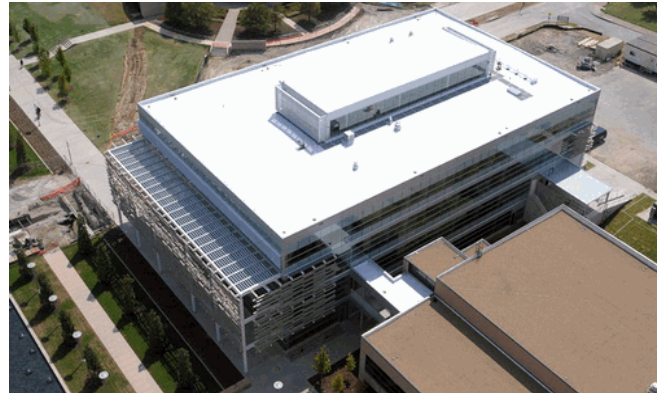

Project Information

Project Status:	Active
Project Delivery Method:	Construction Manager at Risk
CIP Project Type:	New
Gross and Assignable Square Feet:	GSF: 74,343 ASF: 54,331
"44 Initiative" Project:	No
Phase and Estimated % Complete:	Warranty - 79%
OFPC RPM, SPM, PM, RCM, IM:	Salcher, Lund, Naylor, Yauger, Connolly
Architecture Firm:	Perkins + Will
Construction Firm:	Hill & Wilkinson

Project Budget

Construction Services:	\$ 20,049,765	at \$ 269.69 / GSF
Total Project Cost:	\$ 27,500,000	at \$ 369.00 / GSF

Project Funding

Revenue Financing System Bonds	\$ 27,500,000
--------------------------------	---------------

Project Schedule

BOR/Chancellor DD Approval	02/12/2009
Issue NTP - Construction	05/05/2009
Achieve Substantial Completion	07/21/2010
Achieve Operational Occupancy	08/11/2010

Project Remarks

1. Substantial completion achieved on July 21, 2010.
2. Completion of punch list items inside the building is nearing completion
3. Expanded site construction work is due to last into mid November
5. Change Orders #1, #2 and #3 & #4 have been executed. FF&E Budget is fully funded.
6. FF&E installation is complete except for punch list items.
7. Landscaping Substantial Completion achieved on 11/11/2010 at 1:30 pm.
8. Final Completion achieved on 12/17/2010.

Board Approvals

None
